


SENTRI-GATE EXAMPLE

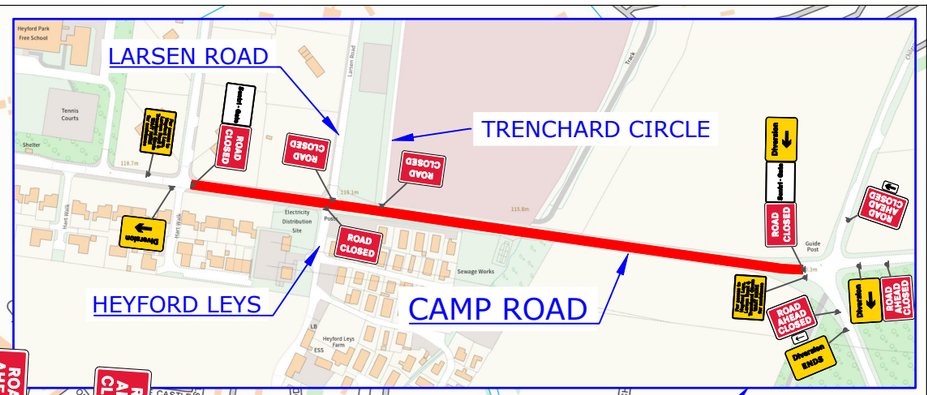

SOMERTON ROAD

STATION ROAD

CAMP ROAD

CAMP ROAD

CAMP ROAD

UNNAMED SINGLE CARRIAGEWAY 6808672

B4030 STREET FROM LOWER HEYFORD TO CAULCOTT

B4030 LOWER HEYFORD ROAD

B4030 HEYFORD ROAD

Upper Heyford

Caulcott

Old Steam Mill Cottage

Lime Hollow

Timberyard Clump

New Nursery

Park Farm

The Gorse

The Heath

Nut Tree Spinney

Education Facility

Museum

GULLY CLEANER / JETTER IN USE

UNABLE TO MAINTAIN LANE WIDTH FOR SHUTTLE WORKING DUE TO LOCATION OF ACCESS POINTS AT PINCH / PRIORITY LOCATION

ONSITE TMO'S TO MANAGE ACCESS TO / FROM PRIVATE STREETS WITHIN CLOSURE POINTS

What3Words///
foresight.unrated.allies
to
during.accompany.snippets

Diversion Length:
5.0 Miles

Special Signs

For access to Heyford Leys, Larsen Road & Trenchard Circle WAIT HERE for assistance x2

No through route x2

RADIOS REQUIRED
TM to Provide
Openreach Engineer
With Radio.

WORKS AREA TO BE AIR LOCKED AND PATROLLED FOR PEDESTRIANS BY ONSITE TMO

All properties within Closure points to be leaflet dropped

ADVANCED WARNING

Advanced Warning ROAD CLOSED HERE ON XX/XX/XX FOR XX DAYS FROM XX:XX TO XX:XX

ROAD CLOSED

ROAD CLOSURE

DIVERSION ROUTE

ROAD CLOSURE LENGTH	450 METRES
ROAD CLOSURE WIDTH	3.5 METRES

Contract No	213-S018542	Client: OPENREACH	
Date	12/02/2026	Site Location / Drawing Title	
Drawn by	DFP/213	CAMP ROAD	
Approved By	DFP/213	UPPER HEYFORD	
Purpose of works	Telecoms works	BICESTER	
Version Number	001	OXFORDSHIRE	
Amended By		OX25 5TA	
Amendment Date		Scale	NOT TO SCALE
Sheet No	1 of 1	OS Licence No	0000000000000

Note
1. All equipment shall be approved and shall comply with the Department Of Transport specification MCE0111. This drawing does not show the normal road works signage that will be required as per Chapter 8.
2. All signs to be in accordance with TSRGD 2016 and to minimum class retroflective.
3. Minimum height of lettering to be 60mm and sign boards to be 1000mm (750mm where appropriate).


The information in this drawing may not be copied or used by third parties without written consent from Sunbelt Rentals ltd (Traffic Management).
This layout is for installation by NRSWA, Lantra 12A,12B,12C,12D qualified persons.
All works shall be in accordance with Safety at Street Works and Road Works, A Code of Practice 2013 & Chapter 8

TO BE INSTALLED AT CLOSURE POINTS



THIS DOCUMENT IS UNCONTROLLED WHEN PRINTED
The electronic version of this document is the approved and most current. Any printed version is uncontrolled and may not be current.

DETAIL AL (AL)
Manned Airlock system.
Notes:
1) Minimal site traffic 25 - 30m air lock is sufficient, Extend airlock for larger work vehicle flow.
2) Red lamps to be used on Nissen Barrier (all HE netwoks)



V01

SUNBELT RENTALS
Sunbelt Rentals UK (Traffic Management)
Kemble Airfield Enterprise Park,Cirencester Road, Kemble GL7 6BQ
Telephone: 0370 050 0792
